




ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names	Jun 3, '18					
							W	T	F	S	S	M
1		Rochambeau (Anderson's corner)	15 days	Mon 7/16/18	Fri 8/3/18							
2		right shoulder	5 days	Mon 7/16/18	Fri 7/20/18	Howard Brothers						
3		Concrete repair (right lane)	5 days	Mon 7/23/18	Fri 7/27/18	Denton						
4		Concrete repair (left lane)	5 days	Mon 7/30/18	Fri 8/3/18	Denton						
5		<New Task>										
6		Route 199 E Bound	8 days	Sun 7/22/18	Tue 7/31/18							
7		Milling & Paving (night)	5 days	Sun 7/22/18	Thu 7/26/18	Branscome						
8		Signal Loops	2 days	Mon 7/30/18	Tue 7/31/18	Brook Hill						
9		Striping	2 days	Mon 7/30/18	Tue 7/31/18	Spivey						
10		Rochambeau (Bruton)	5 days	Mon 7/23/18	Fri 7/27/18							
11		Shoulder widening	5 days	Mon 7/23/18	Fri 7/27/18	Howard Brothers						
12		Route 60 (tentative)	4 days	Sun 7/29/18	Thu 8/2/18							
13		Milling & Paving (night)	5 days	Sun 7/29/18	Thu 8/2/18	Branscome						

Project: 2018.07.19 N31 look ah
Date: Thu 7/19/18

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

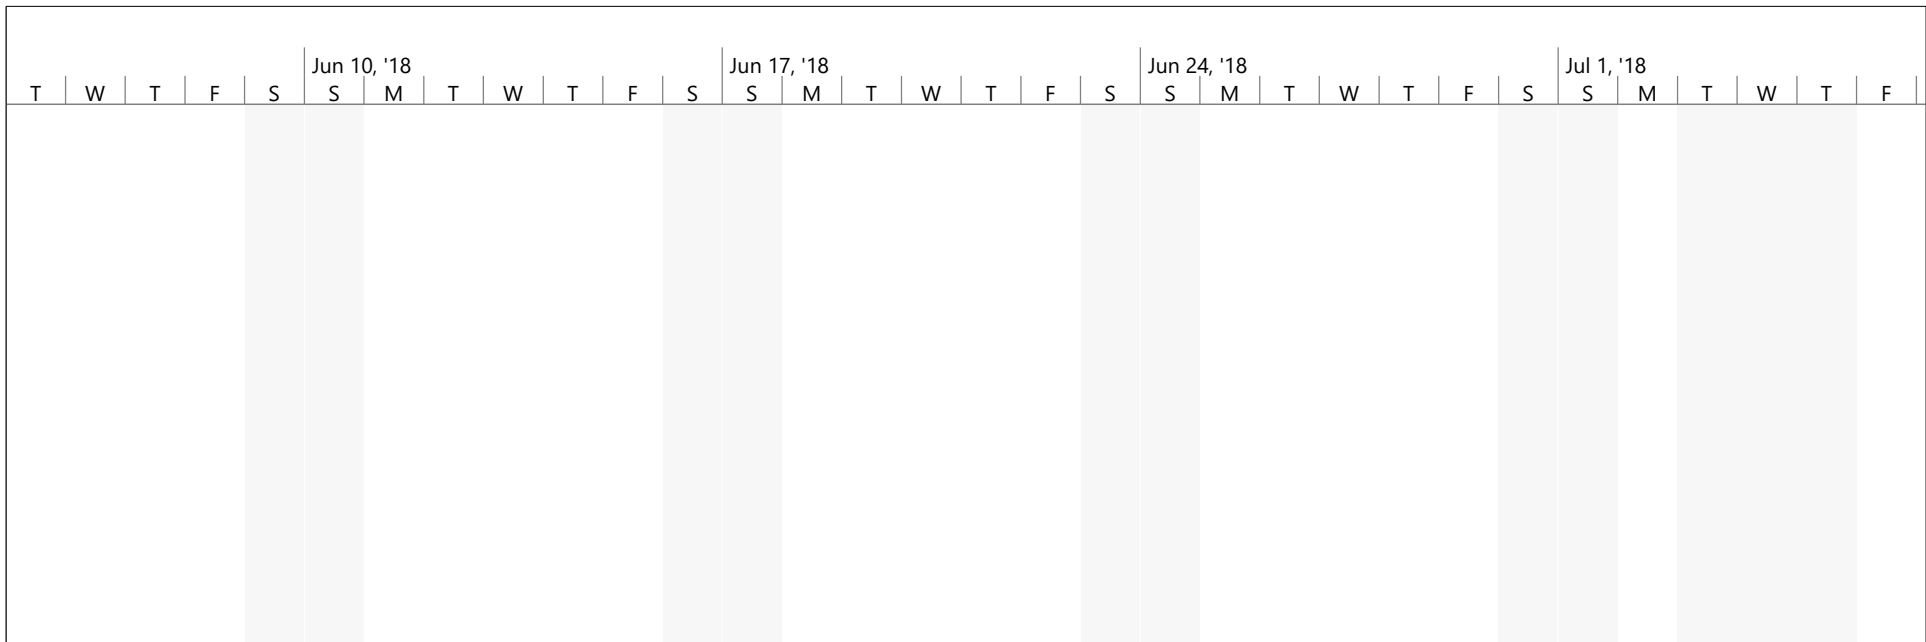

Project: 2018.07.19 N31 look ah Date: Thu 7/19/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

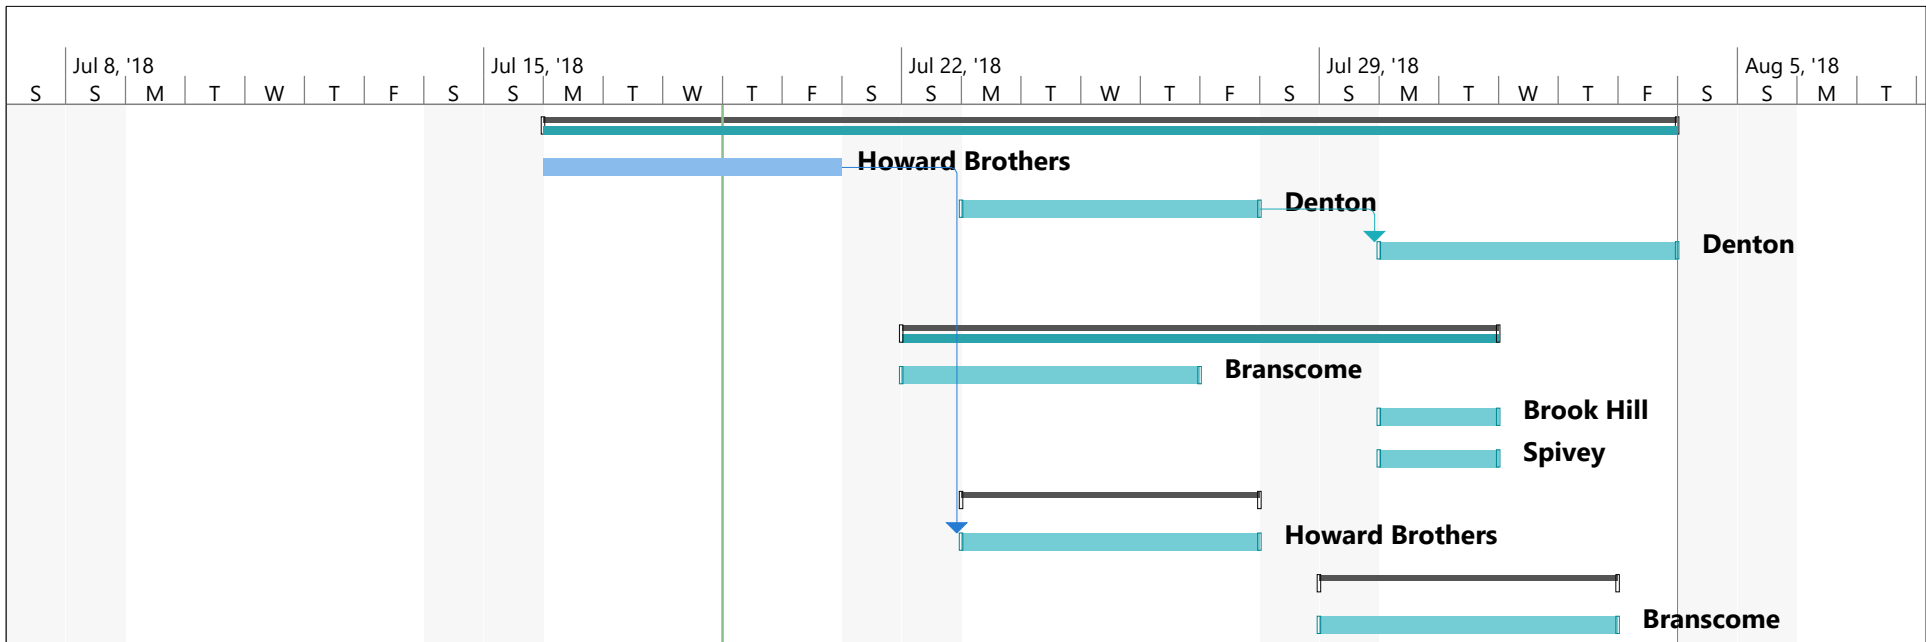

Project: 2018.07.19 N31 look ah Date: Thu 7/19/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
